Citizens' Oversight Committee Meeting

2017 FWISD Capital Improvement Program

Presented By: PROCEDEO

August 27, 2018



Agenda



- Program Overview
- Operational Excellence (OPEX)
- Financial Overview
- Project Schedule
- Communications
- HUB Update

Operational Excellence



OPEX

Click to website


Financial Overview



Job No	Job Description	Budget	Committed	Uncommitted
	ESCALATION	67,784,163.00	0.00	67,784,163.00
	REIMBURSEMENT RESOLUTION	7,895,000.00	0.00	7,895,000.00
	LAND PURCHASE	16,000,000.00	7,145,488.30	8,854,511.70
082	BIOMEDICAL SCIENCE	4,000,000.00	3,264,090.74	735,909.26
084	WORLD LANGUAGES INSTITUTE	1,000,000.00	657,749.70	342,250.30
	ADMIN/OPERATIONAL COSTS	19,910,205.00	2,333,709.61	17,576,495.39
	FWISD PROJECT TOTAL	116,589,368.00	13,401,038.35	103,188,329.65
001	CARTER RIVERSIDE HS	48,187,902.00	4,583,439.38	43,604,462.62
002	ARLINGTON HEIGHTS HS	51,329,625.00	4,945,302.58	46,384,322.42
003	SOUTH HILLS HS	51,182,661.00	4,912,965.72	46,269,695.28
004	DIAMOND HILL HS	28,512,553.00	2,773,324.05	25,739,228.95
005	DUNBAR HS	32,932,975.00	3,253,418.71	29,679,556.29
006	EASTERN HILLS HS	46,764,698.00	4,572,554.80	42,192,143.20
800	NORTH SIDE HS	34,090,276.00	3,402,822.23	30,687,453.77
009	POLY HS	49,500,995.00	4,750,634.39	44,750,360.61
010	PASCHAL HS	40,054,076.00	6,695,882.85	33,358,193.15
011	TRIMBLE TECH HS	39,328,489.00	3,745,695.49	35,582,793.51
014	SOUTHWEST HS	40,731,603.00	3,945,718.77	36,785,884.23
015	WESTERN HILLS HS	32,143,080.00	3,148,604.82	28,994,475.18
016	OD WYATT HS	41,205,538.00	4,000,028.94	37,205,509.06
071	BENBROOK MS/HS	27,328,394.00	2,715,630.51	24,612,763.49
083	NEW YOUNG MENS LEADERSHIP ACAD	34,763,490.00	2,930,736.78	31,832,753.22
171	TANGLEWOOD ES RENO	5,817,073.00	223,143.44	5,593,929.56
176	WAVERLY PARK ES RENO	2,090,510.00	226,100.17	1,864,409.83
229	TANGLEWOOD NEW RELIEF LOCATION	27,181,694.00	2,372,492.14	24,809,201.86
	TOTAL COMMITED JOB RELATED	633,145,632.00	63,198,495.77	569,947,136.23
	GRAND TOTAL CIP 17	749,735,000.00	76,599,534.12	673,135,465.88


FWISD 2017 Bond



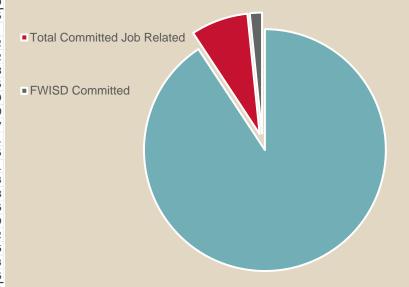

Schedule



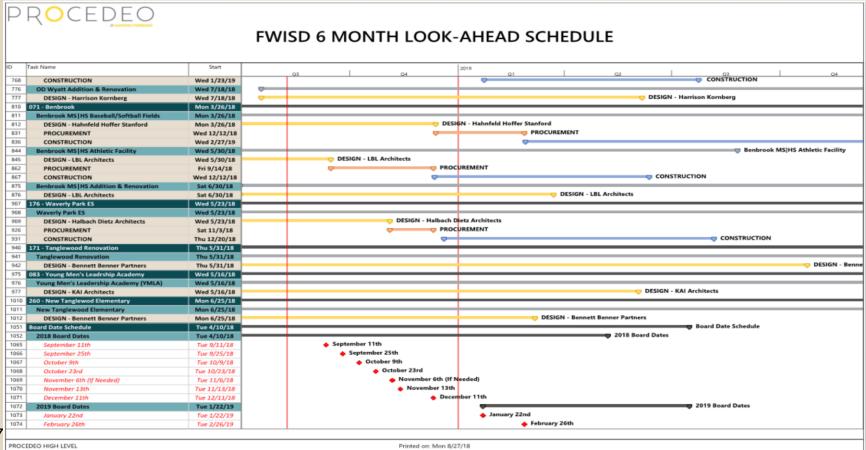

Bid Schedule



Projects Bidding between October 2018 – March 2019 (14 Projects)

- Amon Carter-Riverside Athletics
- Arlington Heights Athletics
- Benbrook Athletics
- Benbrook Baseball-Softball
- Dunbar Athletics
- Eastern Hills Athletics
- North Side Athletics


- North Side Mariachi Band
- OD Wyatt Athletics
- Poly Athletics
- South Hills Athletics
- Southwest Athletics
- Waverly Park Elementary Renovation
- Western Hills Athletics

Communications – FWISD 2017 Bond Website



Completed

- All 2017 Bond projects live on website
- Filters
 - In Design
 - Under Construction
 - Complete
- "Design" and "Construction" progress bars
- Monthly "Construction Updates"
- Cosmetic changes to create a better experience (ex. colors, animation)






CONSTRUCTION UPDATE

August 20, 2018

Finishing walls, ceilings and floors. Every week we get a little bit closer!

FWISD 2017





In Progress

- FAQ Page
- E-newsletter
- Social media
- Using web analytics to improve website


Communications – Bid Preview Event





HUB Program ReportOverall HUB Participation



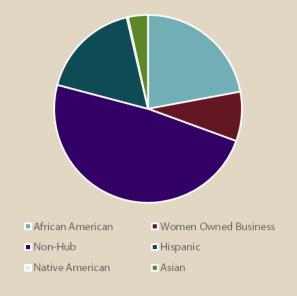

COMMITTE 52P49

%

HUB contracts to date

